
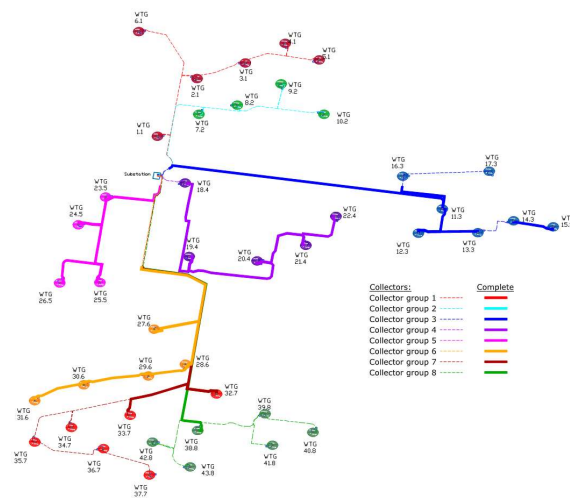


SUMMARY OF TASKS LAST WEEK

- Subgrade preparation in MC19, WTG 16
- Pavement in MC05, MC09, MC19, MC28, WTG's 10, 17, 31, 38, 41
- Foundation excavation WTGs 17
- Anchor cage in WTG 4, 5, 8
- Blinding in WTG 9, 10
- Steel works in WTGs 2, 3, 5, 8, 36
- Concrete pour WTG's 7, 3, 36
- Backfill of WTG 1, 31, 33, 34
- Earthing in WTG 3, 7, 36
- Trenching cables in WTG 23-sub, WTG 29-30, WTG 30-31
- Turbine component deliveries to WTG 20, 21, 25, 30
- Turbine component install WTG 19

SUMMARY OF TASKS THIS WEEK

- Pavement in MC19, MC28
- Anchor cage in WTG 9, 10
- Steel works in WTGs 4, 5
- Concrete pour WTG 36
- Backfill of WTG's 6
- Trenching cables in CG 6, 7, 8 - Sub
- Pour of equipment footings
- Precast culvert installation
- Installation of transformer 1 & 2
- Installation of switchyard equipment
- Excavation of oil & water separator
- Installation of the switch room building

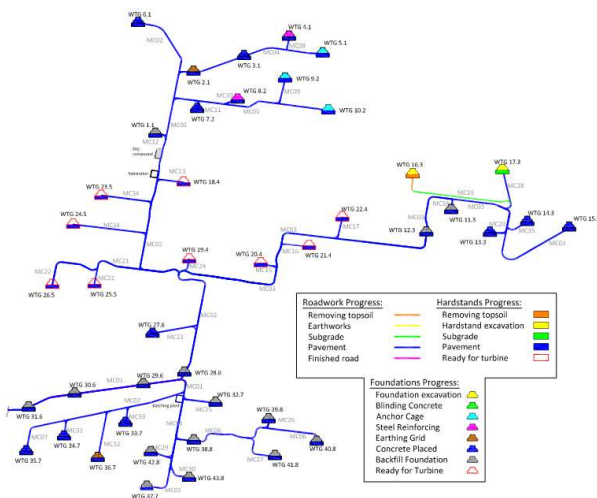

Legend:

- Conduits
- Excavation
- Blinding
- Reinforcement
- Concrete
- Equipment assembly

