


SUMMARY OF TASKS LAST WEEK

- Subgrade preparation in MC19
- Pavement in MC05, MC09, MC19, MC28, WTG's 16, 17, 31, 33, 38, 41
- Culvert installation MC11-1, MC31-1, MC32-1, MC35-1, MC03-9
- Anchor cage in WTG 9, 10, 17
- Blinding in WTG 16, 17
- Steel works in WTGs 8, 4, 5, 9, 10
- Concrete pour WTG's 36, 2, 8
- Backfill of WTG 6, 3, 34
- Earthing in WTG 2, 4, 5, 8, 10
- Trenching cables in WTG 23-sub, WTG 39-40, WTG 30-31

SUMMARY OF TASKS THIS WEEK

- Anchor cage in WTG's 16, 17, 9
- Steel works in WTGs 4, 16, 17, 9
- Concrete pour WTG 4, 5, 9, 10
- Backfill of WTG's 3, 2, 5, 34, 36, 7
- Trenching cables in CG 5, 6, 7, 8
- Stairs in WTG's 3, 2, 34, 36, 7
- Earthing in WTG's 4, 9, 10, 5
- Pour of equipment footings
- Installation and preparation of transformer 1 & 2
- Installation of switchyard equipment
- Excavation and foundation of oil & water separator
- Installation of the switch room building

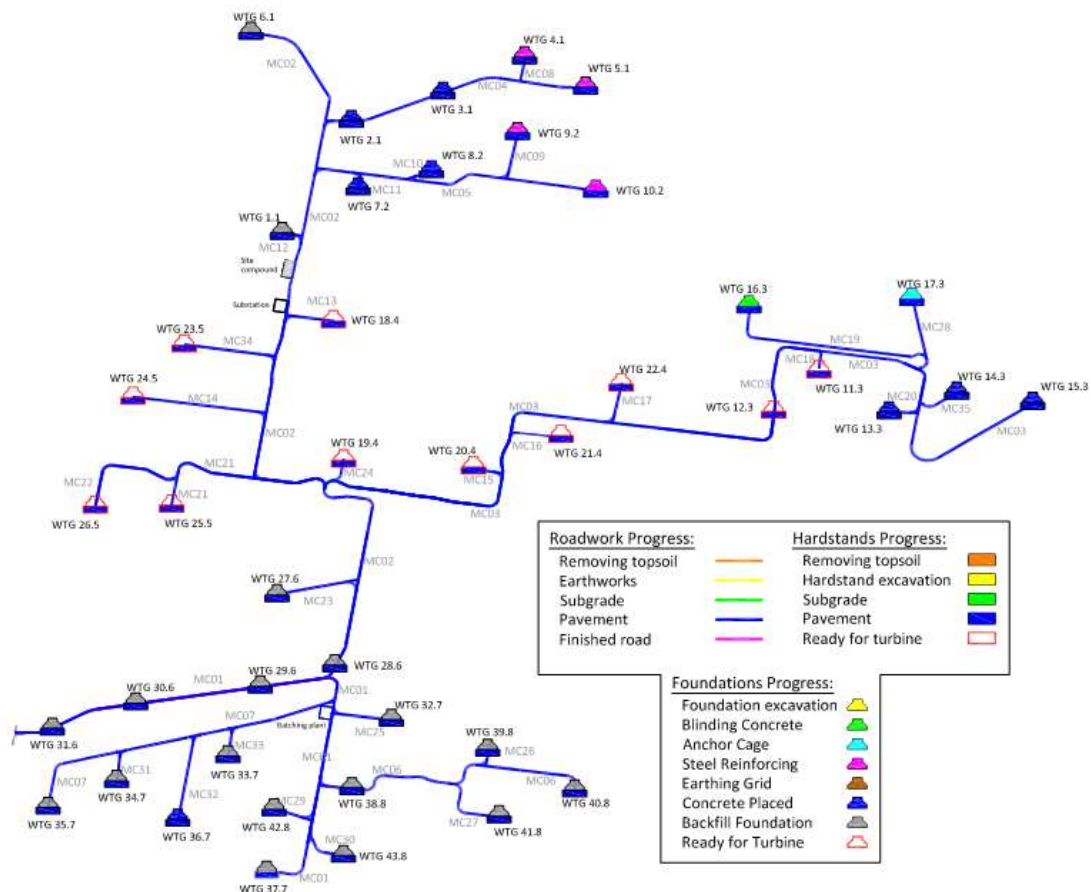

	Completed	Total	%
Foundations	37	43	86%
Roads (m)	33,452	38,027	88%
Cable (m)	30,543	64,055	48%
