


SUMMARY OF TASKS LAST WEEK

- Pavement in MC04, MC05, MC09, WTG's 3, 8, 4, 5
- Culvert installation MC35-1, MC03-9
- Anchor cage in WTG 16
- Steel works in WTGs 4, 9, 16, 17
- Concrete pour WTG's 5, 4, 9, 10
- Backfill of WTG 3, 34, 36, 7, 8
- Earthing in WTG 4, 5, 9, 10, 17, 16
- Trenching cables in WTG 39-40, WTG 39-41, WTG 42-43


SUMMARY OF TASKS THIS WEEK

- Pavement in MC03, MC15
- Steel works in WTGs 16
- Concrete pour WTG 17, 16
- Backfill of WTG's 2, 4, 5, 8
- Trenching cables in CG 8
- Stairs in WTG's 2, 4, 5, 8
- Earthing in WTG's 16, 17


	Completed	Total	%
Foundations	41	43	95%
Roads (m)	34,838	38,027	92%
Cable (m)	33,254	64,055	52%

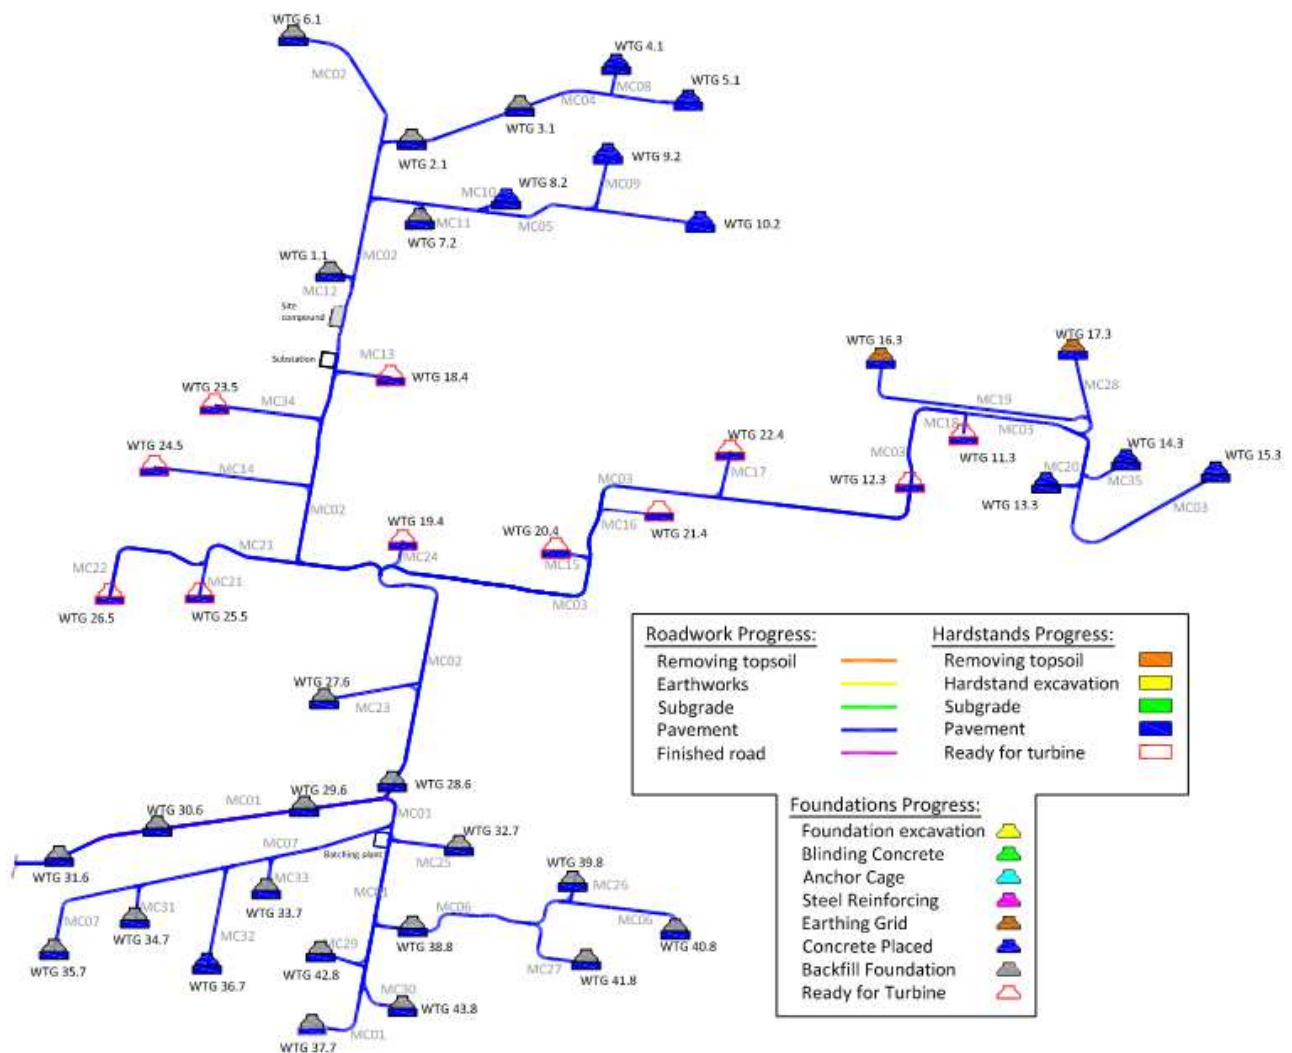

MV Underground Cable

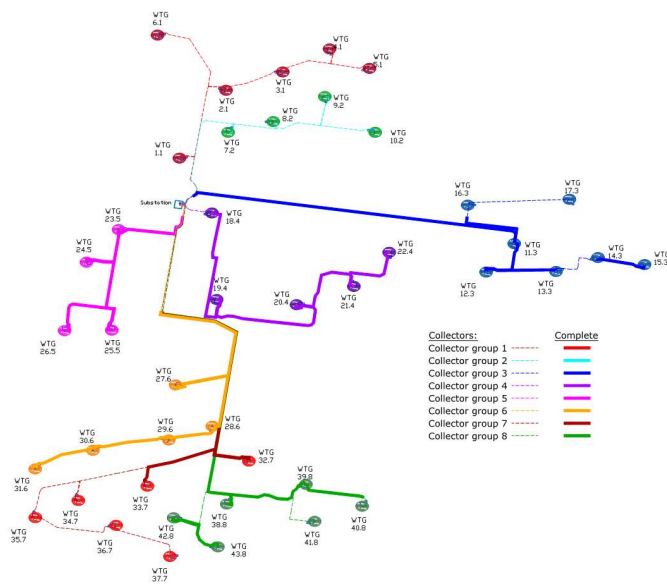

Off-Site Substation

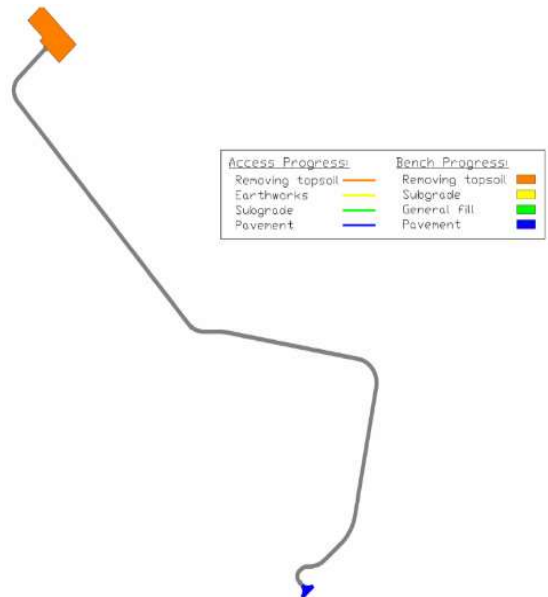

Sub-Station



Legend:

- Conduits
- Excavation
- Blinding
- Reinforcement
- Concrete
- Equipment assembly

