Ryan Corner Wind


Farm

Weekly Construction Report January 30, 2023



Another foundation pour, access tracks being built, foundations being excavated and cabling continuing. Some of the activities on site this last week.

5 foundations have been poured.

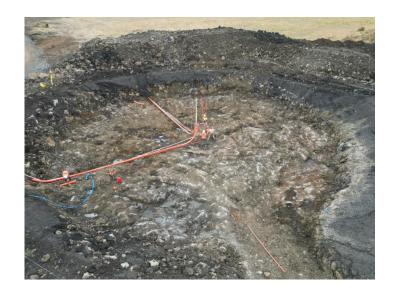

Connections:

The collector substation earthworks bench at Ryan Corner are well underway and should be completed by the end of February.

The foundations at the Tarrone terminal station are completed and structures are being assembled.





What does the dental crew do?:

The dental crew clean the excavated foundation of excess loose rock and soil in preparation for the blinding pour and any flowable fill. The initial concrete pour levels the surface prior to the main foundation pour. Conduit and cabling are put in place before any concrete is placed in the foundations.

